The Middlesex Corporation

Input Date of First Monday

3/2/2026

90 Day Look Ahead

Item #	Activity Description	Start Date	Working Days	End Date	Shift	State Police	Local Police	MNR Support
	Look Ahead Schedule							
	Project							
	Replacement of Bridges 00161 & 00162							
	Construction							
	Install/Repair Silt Fence site wide as Needed	**5-Jan-26**	70	4/10/2026				
	Install Temp Lighting (ETC)	**12-Feb-26**	20	3/11/2026		2		
	Install DS- 33	**7-Mar-26**	1	3/7/2026	Night			
	Install DS- 50 and Pipe	**23-Mar-26**	4	3/24/2026				
	Install DS-56 and Pipe	**25-Mar-26**	6	3/30/2026				
	Flow Fill CB Under Bridge by ABT 1 Bridge 162	**31-Mar-26**	2	4/1/2026				
	Full Depth Road Construction 96+80-101+03 &102+14-107+25	**20-Apr-26**	15	5/8/2026				
	DS-3, 3A,3B	**30-Apr-26**	5	5/6/2026				
	Earthwork/Grading From Bridge 161 to Western Limit	**3-May-26**	10	5/14/2026				
	Paving Base Course From Bridge 161 to Westerm Limit	**18-May-26**	5	5/22/2026				
	Bridge 00162							
	Install Temp Crane Access	**29-Mar-26**	10	4/9/2026				
	Flood Tracks	**22-Mar-26**	5	3/26/2026	Night			
	Install Timber shielding above MNR Row	**31-Mar-26**	20	4/27/2026	Night	2		Yes
	Erect Steel Girders and Diaphrams During Outages- Weekend 1	**10-Apr-26**	2	4/11/2026	Night	2		Yes
	Erect Steel Girders and Diaphrams During Outages- Weekend 2	**17-Apr-26**	2	4/18/2026	Night	2		Yes
	Erect Steel Girders and Diaphrams During Outages- Weekend 3	**24-Apr-26**	2	4/25/2026	Night	2		Yes
	Erect Steel Girders and Diaphrams During Outages- Weekend 4	**1-May-26**	2	5/2/2026	Night	2		Yes
	Survey- Haunch Grades	**4-May-26**	4	5/7/2026				
	F&P Keepers	**8-May-26**	2	5/11/2026				
	Install SIP/Haunch angle/Studs	**10-May-26**	4	5/13/2026	Night	2		Yes
	Install Deck Rebar	**14-May-26**	10	5/27/2026				
	Form Deck Ends	**12-May-26**	8	5/21/2026				
	Set Bidwell/ Dry run	**27-May-26**	2	5/28/2026				
	Abutment 1							
	Place FGA	**2-Feb-26**	35	3/20/2026				
	Install Panels and Light Weight Wall 102	**13-Feb-26**	20	3/12/2026				
	Build Access Road for Wall 101	**13-Feb-26**	40	4/9/2026				
	Excavate for Level Pad Wall 101	**28-Mar-26**	50	6/5/2026				
	Install Underdrain Wall 101	**28-Mar-26**	50	6/5/2026				
	Install Wall Panels	**31-Mar-26**	45	6/5/2026				
	Backfill with 3/4" Stone	**31-Mar-23**	45	6/5/2026				
	Install Bridge Bearings	**31-Mar-26**	2	4/1/2026				
	Abutment 2							
	Install FGA	**2-Feb-26**	40	3/27/2026				
	Install Wire Relief Wall	**2-Feb-26**	35	3/20/2026				
	Strip Forms and Demobilize	**2-Mar-26**	6	3/7/2026				
	Damp Proof For Abutment Top Section	**11-Mar-26**	2	3/12/2026				
	Complete Approach MSE Wall 201 Abt 2	**13-Mar-26**	7	3/19/2026				
	Install Crane Matting on FGA	**31-Mar-26**	6	4/5/2026				
	Install Bridge Bearings	**31-Mar-26**	2	4/1/2026				
	Bridge 00161							
	Abutment 1							
	Complete Abutments/Wingwalls/Sacrificial CMU Block	**2-Feb-26**	50	4/10/2026				
	Form Distribution Slab & Wall Coping	**24-Mar-26**	5	3/30/2026				
	Install Rebar Distribution Slab	**30-Mar-26**	6	4/6/2026				
	Place Distribution Slab & Coping	**6-Apr-26**	4	4/9/2026				
	Cure Distribution Slab & Coping	**9-Apr-26**	7	4/17/2026				
	Install Bridge Bearings	**9-Apr-26**	1	4/9/2026				
	Erect Steel Beams and Diaphram's	**21-Apr-26**	4	4/26/2026	Night	2	2	
	Install Deck Pans	**6-May-26**	5	5/12/2026	Night	2	2	
	Install Deck Rebar	**12-May-26**	14	5/29/2026				
	Form Deck and End Diaphrams	**29-May-26**	5	6/4/2026				
	Abutment 2							
	Complete Abutments/Wingwalls/Sacrificial CMU Block	**2-Feb-26**	30	3/13/2026				
	Form Distribution Slab & Wall Coping	**13-Mar-26**	5	3/19/2026				
	Install Rebar Distribution Slab	**19-Mar-26**	6	3/26/2026				
	Place Distribution Slab & Coping	**26-Mar-26**	2	3/27/2026				
	Cure Distribution Slab & Coping	**27-Mar-26**	7	4/6/2026				
	Install Bridge Shims	**15-Apr-26**	2	4/16/2026				
	Erect Steel Beams and Diaphram's	**21-Apr-26**	4	4/26/2026	Night	2	2	
	Install Deck Pans	**6-May-26**	5	5/12/2026	Night	2	2	
	Install Deck Rebar	**11-May-26**	14	5/29/2026				
	Form Deck and End Diaphrams	**25-May-26**	5	5/29/2026				
	Retaining Walls							
	Wall 201 Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**2-Feb-26**	48	4/7/2026				
	Wall 202 Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**2-Feb-26**	48	4/7/2026				
	Wall 102 Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**2-Feb-26**	50	4/10/2026				
	Wall 101 Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**23-Feb-26**	70	5/29/2026				
	Wall 302 Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**28-Mar-26**	45	5/28/2026				
	Wall 501 Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**18-May-26**	30	6/26/2026				
	Subcontractors							
	Designs by Ilde - Silt Fence							
	Alvarez- Rebar Installation							
	ETC- Temp Lighting							
	Structural Services-SIP Forms/Studs							

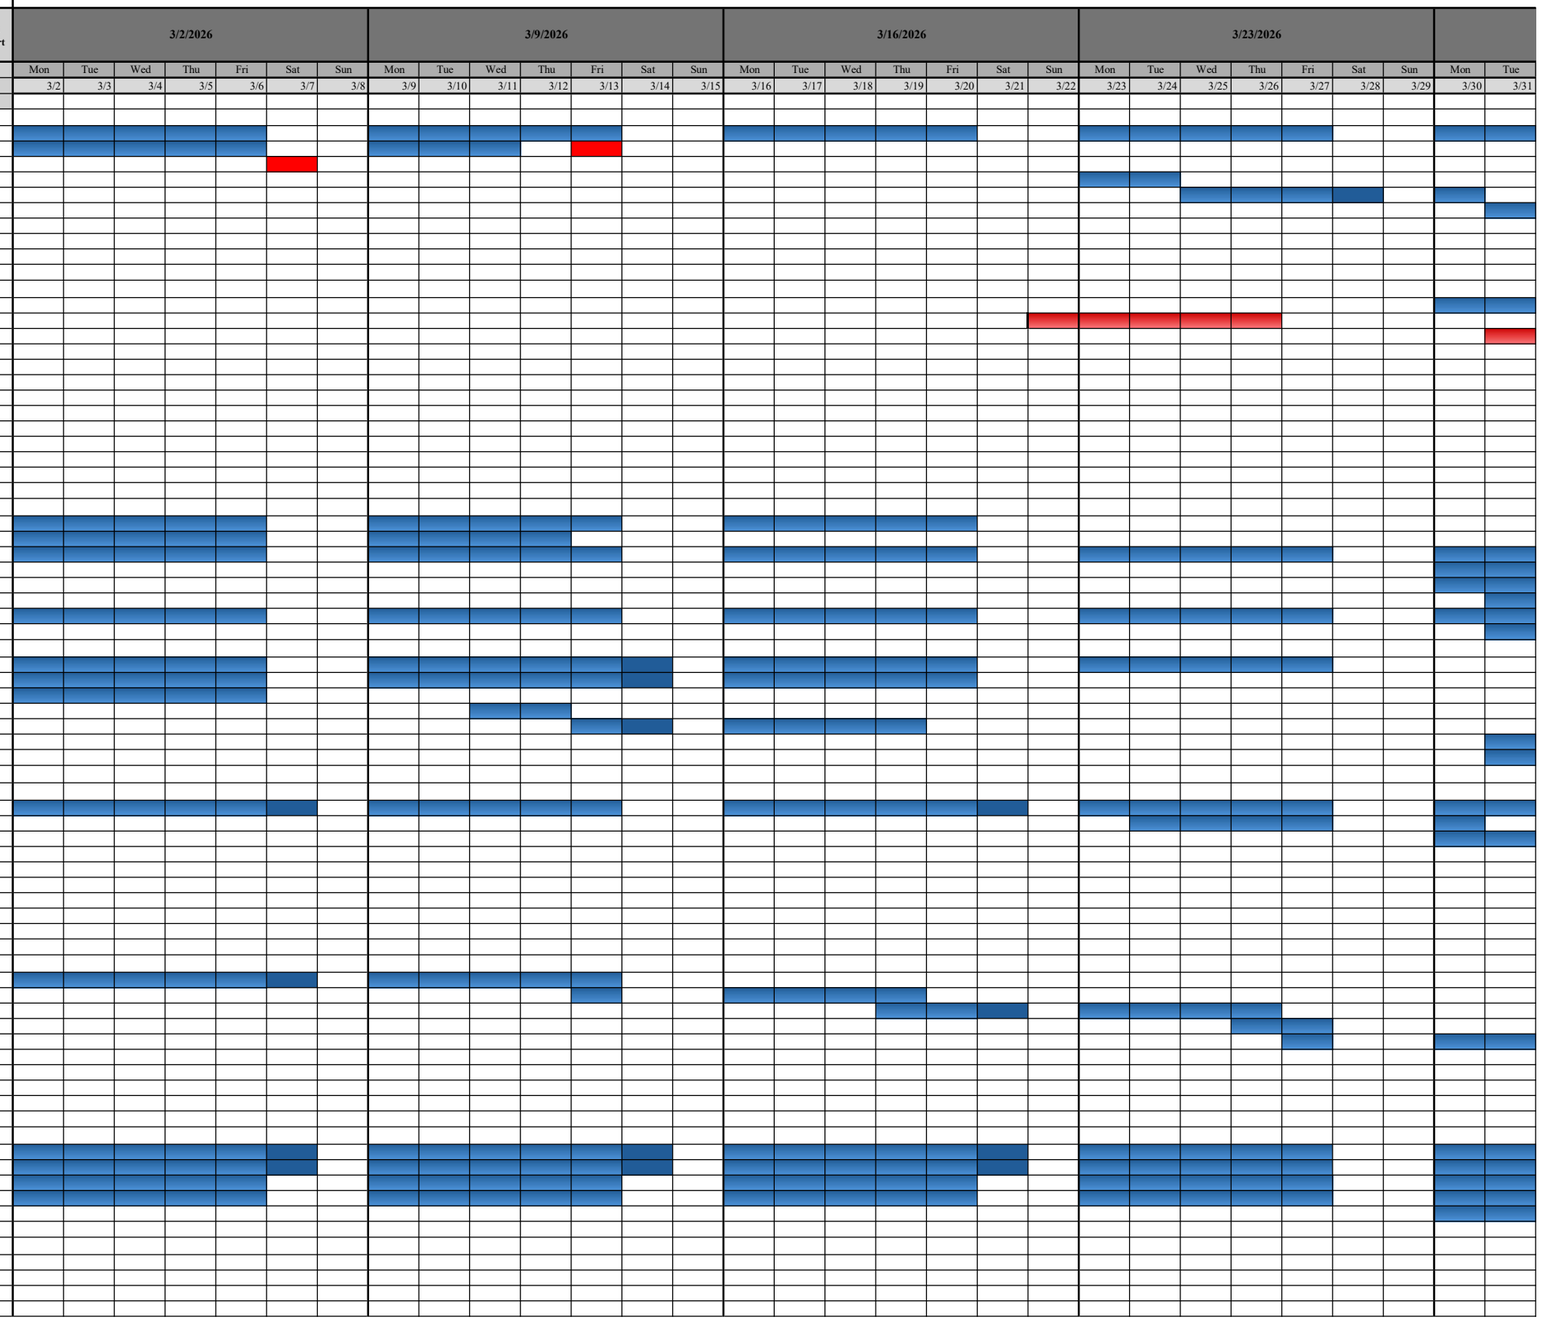

3/30/2026					4/6/2026							4/13/2026							4/20/2026							4/27/2026							5/4/2026							5/11/2026					
Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat
4/1	4/2	4/3	4/4	4/5	4/6	4/7	4/8	4/9	4/10	4/11	4/12	4/13	4/14	4/15	4/16	4/17	4/18	4/19	4/20	4/21	4/22	4/23	4/24	4/25	4/26	4/27	4/28	4/29	4/30	5/1	5/2	5/3	5/4	5/5	5/6	5/7	5/8	5/9	5/10	5/11	5/12	5/13	5/14	5/15	5/16

Good Friday

	5/18/2026							5/25/2026							6/1/2026							6/8/2026							6/15/2026							6/22/2026						
Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun
5/17	5/18	5/19	5/20	5/21	5/22	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5	6/6	6/7	6/8	6/9	6/10	6/11	6/12	6/13	6/14	6/15	6/16	6/17	6/18	6/19	6/20	6/21	6/22	6/23	6/24	6/25	6/26	6/27	6/28

Memorial Day
