The Middlesex Corporation

90 Day Look Ahead

Input Date of First Monday

4/6/2026

Item #	Activity Description	Start Date	Working Days	End Date	Shift	State Police	Local Police	MNR Support
	Look Ahead Schedule							
	Project							
	Replacement of Bridges 00161 & 00162							
	Construction							
	Install/Repair Silt Fence site wide as needed	**5-Jan-26**	100	5/22/2026				
	Flowfill Manhole	**7-Apr-26**	1	4/7/2026				
	Permanent Work (ETC)	**13-Apr-26**	60	7/3/2026				
	Full Depth Road Construction 96+80-101+03 &102+14-107+25	**28-Apr-26**	15	5/18/2026	Night	2		
	Install DS-3,3A,3B	**30-Apr-26**	6	5/7/2026	Night	2		
	Install Membrane on RW 201 & RW 202	**3-Jun-26**	5	6/9/2026				
	Earthwork/Grading From Bridge 161 to Western Limit	**3-Jun-26**	10	6/16/2026				
	Paving Base Course From Bridge 161 to Western Limit	**11-Jun-26**	2	6/12/2026				
	Build Water Quality Area 3	**11-Jun-26**	2	6/12/2026				
	Install 12" RCP From DS-39 to CB-13 (44 lf)	**17-Jun-26**	3	6/19/2026				
	Install Stone Stabilization Wall 202 Area	**18-Jun-26**	2	6/19/2026				
	Bridge 00162							
	Install Temp Crane Access	**30-Mar-26**	7	4/7/2026	Night	2		
	Install Steel Plates for Crane Road	**1-Apr-26**	6	4/8/2026				
	Install Timber shielding above MNR Row	**13-Apr-26**	25	5/17/2026	Night	2		Yes
	Setting Steel- Weekend 1	**10-Apr-26**	2	4/11/2026	Night	2		Yes
	Setting Steel- Weekend 2	**17-Apr-26**	2	4/18/2026	Night	2		Yes
	Setting Steel- Weekend 3	**24-Apr-26**	2	4/25/2026	Night	2		Yes
	Setting Steel- Weekend 4	**1-May-26**	2	5/2/2026	Night	2		Yes
	Survey- Haunch Grades	**4-May-26**	4	5/7/2026				
	Install SIP/Haunch angle/Studs	**11-May-26**	4	5/14/2026				Yes
	Form Deck Ends	**12-May-26**	8	5/21/2026				
	Install Deck Rebar	**26-May-26**	10	6/8/2026				
	Install Rebar for Bridge Parapet	**26-May-26**	10	6/8/2026				
	Set Bidwell/ Dry run	**15-Jun-26**	3	6/17/2026				
	Place Bridge Deck Slab	**22-Jun-26**	2	6/23/2026				
	Cure Bridge Deck Slab	**22-Jun-26**	7	6/30/2026				
	F&P Keepers	**24-Jun-26**	2	6/25/2026				
	Abutment 1							
	Place FGA Wall 102, 302	**2-Feb-26**	60	4/24/2026				
	Install Panels and Light Weight Wall 102	**13-Feb-26**	80	6/4/2026				
	Excavate for Level Pad Wall 101	**6-Apr-26**	70	7/10/2026				
	Install Underdrain Wall 101	**6-Apr-26**	50	6/12/2026				
	Backfill with 3/4" Stone	**13-Apr-26**	45	6/12/2026				
	Excavate for Level Pad 302	**13-Apr-26**	30	5/22/2026				
	Install Wall Panels	**13-Apr-26**	50	6/19/2026				
	Set 302 Wall Panels	**14-Apr-26**	30	5/25/2026				
	Wire Wall 102 to 302	**14-Apr-26**	30	5/25/2026				
	Install Formwork Approach/ Moment Slab (West Approach)	**23-Jun-26**	5	6/29/2026				
	Install Rebar for Approach/ Moment Slab	**25-Jun-26**	7	7/3/2026				
	Place Approach/ Moment Slab	**29-Jun-26**	1	6/29/2026				
	Cure Approach/ Moment Slab	**30-Jun-26**	7	7/8/2026				
	Abutment 2							
	Install FGA	**2-Feb-26**	60	4/24/2026				
	Crane set up (BAY)	**8-Apr-26**	3	4/10/2026	Night	2		Yes
	Install Bridge Bearings	**6-Apr-26**	2	4/7/2026				
	Remove Crane Matting	**4-May-26**	5	5/8/2026				
	Install Formwork Approach/ Moment Slab (East Approach)	**23-Jun-26**	5	6/29/2026				
	Install Rebar for Approach/ Moment Slab	**25-Jun-26**	7	7/3/2026				
	Place Approach/ Moment Slab	**29-Jun-26**	1	6/29/2026				
	Cure Approach/ Moment Slab	**30-Jun-26**	7	7/8/2026				
	Bridge 00161							
	Prep Crane Area Bridge 161	**12-Apr-26**	4	4/15/2026	Night	2		
	Install Bridge Shims	**22-Apr-26**	2	4/23/2026				
	Erect Steel Beams and Diaphram's	**22-Apr-26**	2	4/23/2026	Night	2	3	
	Install Deck Pans/ Shear Studs	**28-Apr-26**	5	5/4/2026				
	Install Formwork for Bridge Parapet	**4-May-26**	10	5/15/2026				
	Install Deck Rebar	**12-May-26**	14	5/29/2026				
	Form Deck and End Diaphrams	**26-May-26**	5	6/1/2026				
	Place Bridge Slab	**4-Jun-26**	2	6/5/2026				
	Cure Bridge Slab	**4-Jun-26**	7	6/12/2026				
	Abutment 1							
	Install Rebar Distribution Slab	**31-Mar-26**	8	4/9/2026				
	Place Distribution Slab	**14-Apr-26**	1	4/14/2026				
	Cure Distribution Slab	**14-Apr-26**	7	4/22/2026				
	Place Coping	**26-May-26**	3	5/28/2026				
	Cure Coping	**26-May-26**	7	6/3/2026				
	Abutment 2							
	Cure Distribution Slab	**2-Apr-26**	7	4/10/2026				
	Place Coping	**26-May-26**	3	5/28/2026				
	Cure Coping	**26-May-26**	7	6/3/2026				
	Retaining Walls							
	Wall 201- Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**2-Feb-26**	63	4/29/2026				
	Wall 202- Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**2-Feb-26**	63	4/29/2026				
	Wall 102- Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**2-Feb-26**	80	5/22/2026				
	Wall 101- Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**6-Apr-26**	90	8/7/2026				
	Wall 302- Excavate, Form, Strip, Place, Install and Backfill to Partial Height	**13-Apr-26**	45	6/12/2026				
	Wall 501 Sta 102.79-Sta. 103.53							
	F&P Level Pad Wall 501	**18-May-26**	10	5/29/2026				
	Install Panels	**21-May-26**	8	6/1/2026				
	Install Wall Drainage	**2-Jun-26**	10	6/15/2026				
	Erect Precast Barrier	**16-Jun-26**	6	6/23/2026				
	F&P Moment Slab Wall 501	**24-Jun-26**	8	7/3/2026				
	Subcontractors							
	Designs by Ilde - Silt Fence							
	Alvarez- Rebar Installation							
	ETC- Temp Lighting							
	Structural Services-SIP Forms/Studs							

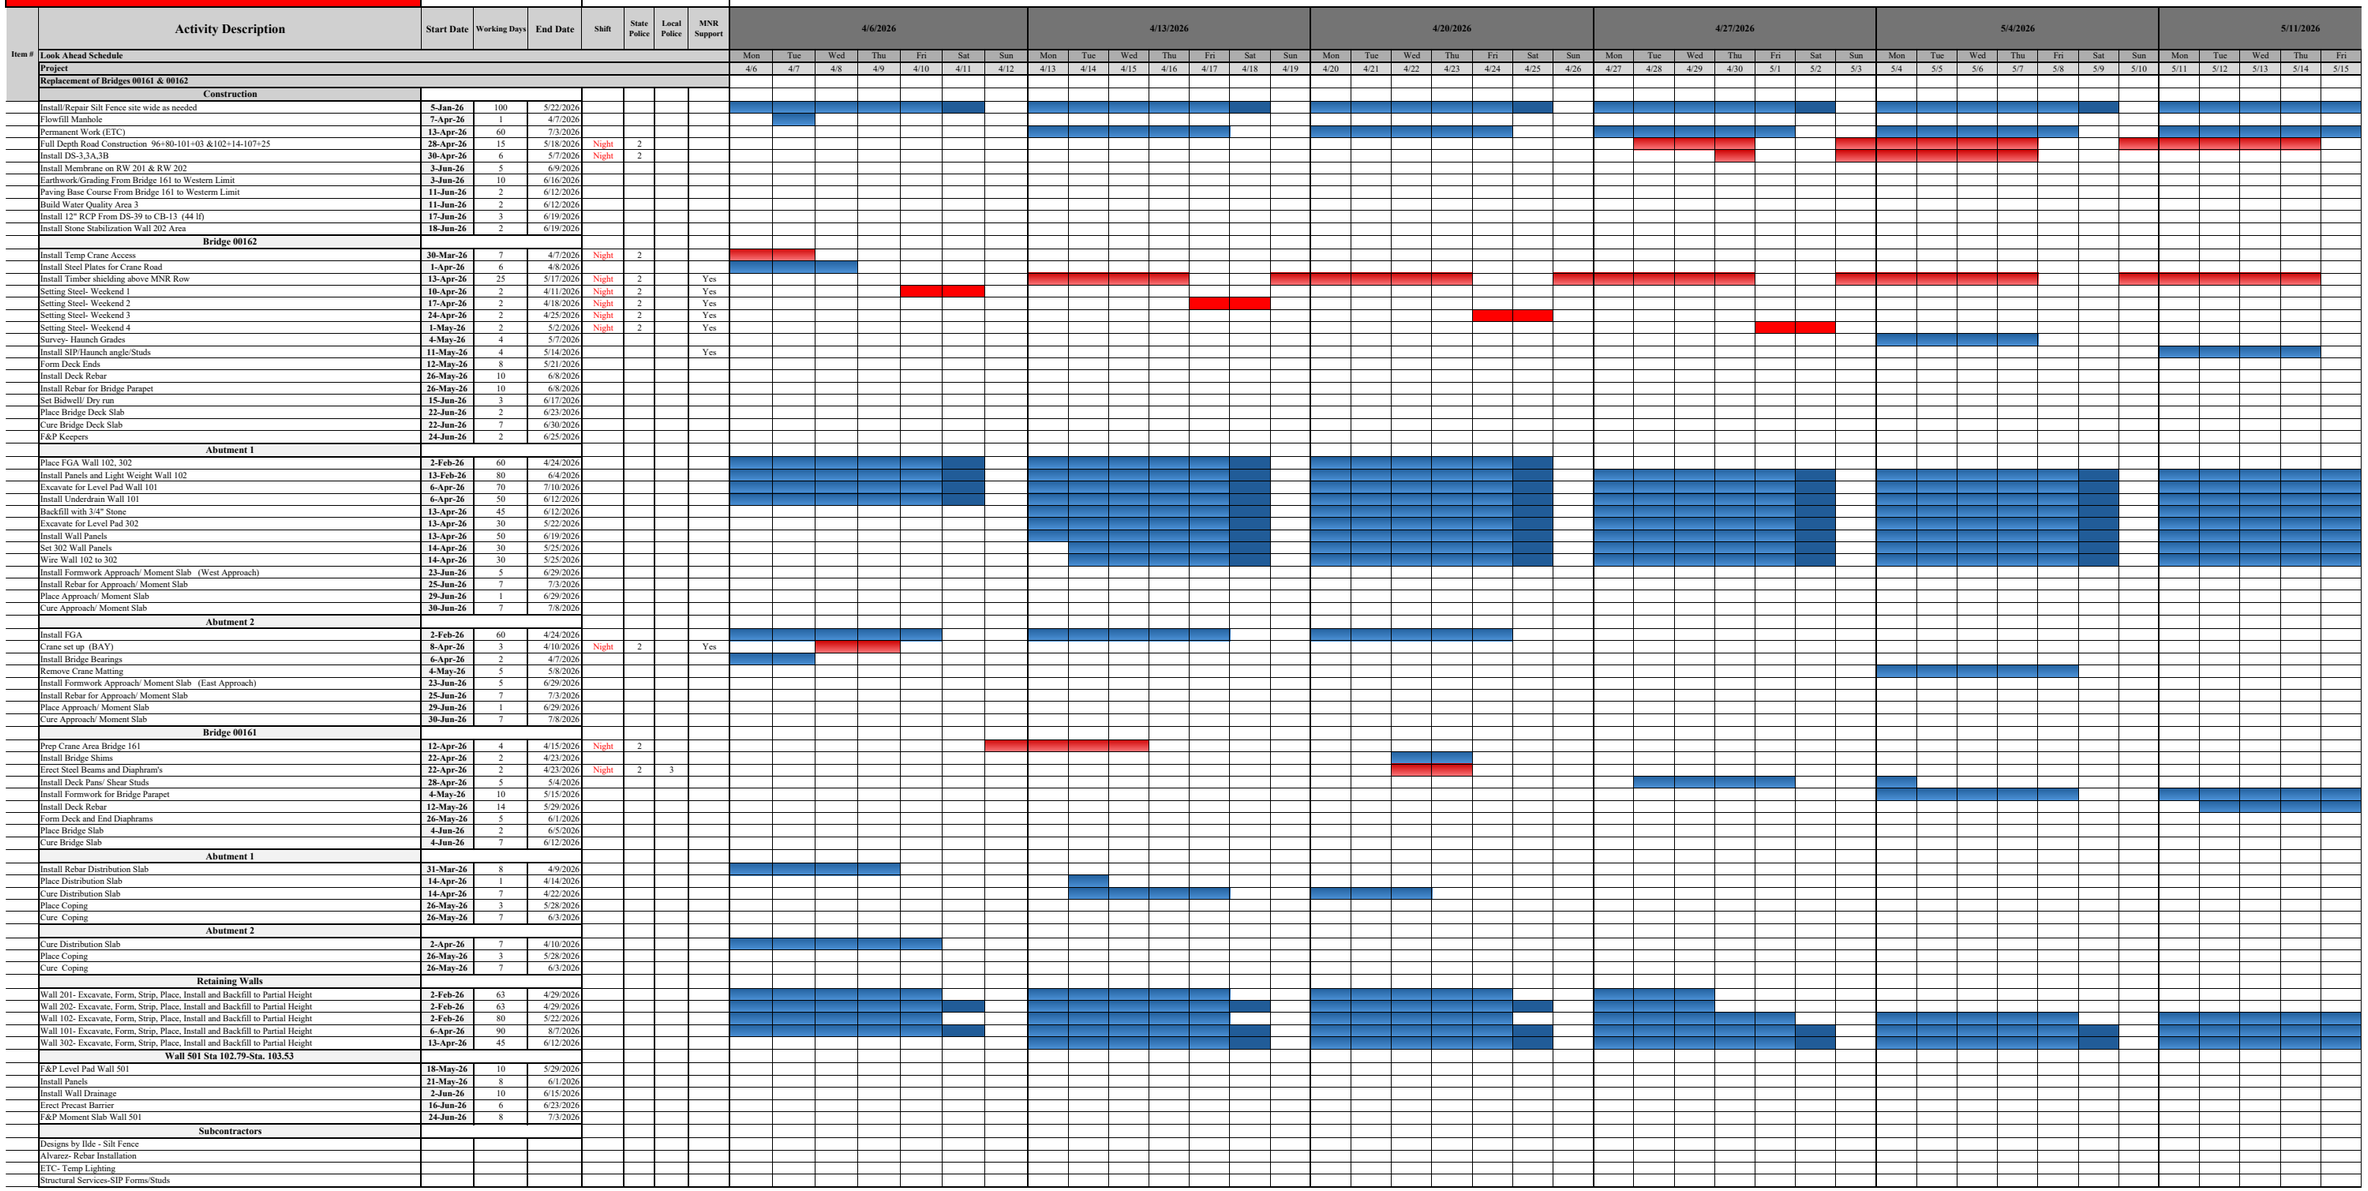

	5/18/2026							5/25/2026							6/1/2026							6/8/2026							6/15/2026							6/22/2026							6/29/2026						
Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun	Mon	Tue	Wed	Thu	Fri	Sat	Sun
5/16	5/17	5/18	5/19	5/20	5/21	5/22	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5	6/6	6/7	6/8	6/9	6/10	6/11	6/12	6/13	6/14	6/15	6/16	6/17	6/18	6/19	6/20	6/21	6/22	6/23	6/24	6/25	6/26	6/27	6/28	6/29	6/30	7/1	7/2	7/3	7/4	7/5

Memorial Day

4th of July Weekend
