The Middlesex Corporation

Input Date of First Monday

7/6/2026

90 Day Look Ahead

Item #	Activity Description	Start Date	Working Days	End Date	Shift	State Police	Local Police	MNR Support
	Look Ahead Schedule							
	Project							
	Replacement of Bridges 00161 & 00162							
	Construction							
	Install/Repair Silt Fence site wide as Needed	**5-Jun-26**	200	10/9/2026				
	Unload Parapet	**7-Jul-26**	5	7/13/2026				
	Saw Cut Asphalt Wall 202 Area	**8-Jul-26**	5	7/14/2026				
	Full Depth Road Recon 1st Ave	**1-Aug-26**	5	8/6/2026				
	Prep Bases For Two Overhead Signs	**12-Aug-26**	10	8/25/2026				
	Drainage							
	Highway							
	CB 3, 3A and 3B and 12" RCP Pipe	**22-Jun-26**	10	7/3/2026				
	Extend RCP for Next Phase DS 3, 33 and 37	**26-Jul-26**	5	7/30/2026	Night	2		
	West Side of Wall 202							
	Water Quality Area 3 Plus Liner	**25-Aug-26**	5	8/31/2026				
	Gore/Grass Area Drainage							
	Install DS 28, 27 and 26	**13-Jul-26**	5	7/17/2026				
	Head Wall Install and RCP across Exit 43 Ramp	**14-Jul-26**	7	7/22/2026				
	West Side of Exit and Through Exit Ramp 43							
	Demo Head Wall and Pipe	**12-Jul-26**	1	7/12/2026				
	Scour Hole and Drainage Across Exit Ramp	**14-Jul-26**	5	7/20/2026				
	First Ave Drainage							
	DS- 42, EX MH 6, 57	**20-Jul-26**	5	7/24/2026				
	Commuter Lot Area							
	DS- 57-17, 17-16, 17-15, 15-14, 13, 19, 18	**1-Aug-26**	10	8/13/2026				
	400' +/- RCP Pipe	**6-Aug-26**	10	8/19/2026				
	Water Quality Area 1 Plus Liner	**19-Aug-26**	5	8/25/2026				
	Bridge 00162							
	Pour Deck Slab	**12-Jul-26**	1	7/12/2026				
	Cure Slab	**12-Jul-26**	10	7/23/2026				
	Place Singular Backwall ABT 1	**16-Jul-26**	1	7/16/2026				
	Cure Backwall	**16-Jul-26**	10	7/29/2026				
	Strip Back Walls	**27-Jul-26**	7	8/4/2026				
	F&P Keepers	**27-Jul-26**	3	7/29/2026				1 Flagger
	Form Bridge Parapets	**13-Jul-26**	15	7/31/2026				
	Place Bridge Barrier (Parapet)	**31-Jul-26**	1	7/31/2026				
	Cure Bridge Barrier (Parapet)	**31-Jul-26**	10	8/13/2026				
	Apply Waterproof Membrane for Slab	**10-Aug-26**	5	8/14/2026				
	Paving for Bridge Deck (Both Sections)	**17-Aug-26**	1	8/17/2026				
	Install Bridge Rail (Fence)	**24-Aug-26**	1	8/24/2026				
	Abutment 1							
	Mass Excavate for Level Pad Wall 101	**6-Apr-26**	70	7/10/2026				
	F&P Level Pad 101	**6-Apr-26**	70	7/10/2026				
	Install Underdrain Wall 101	**6-Apr-26**	70	7/10/2026				
	Install Wall Panels 101	**6-Apr-26**	70	7/10/2026				
	Backfill with 3/4" Stone	**12-Apr-26**	70	7/16/2026				
	F&P Level up Concrete Pad Along Walls	**17-Jul-26**	10	7/30/2026				
	Place FGA Wall 102	**8-Jun-26**	40	7/31/2026				
	Install Panels and Light Weight Wall 102	**8-Jun-26**	35	7/24/2026				
	Install Phase Line Wall	**20-Jun-26**	30	7/30/2026				
	Set Parapet	**27-Jul-26**	17	8/18/2026				
	Install Formwork Approach Slab (West Approach)	**28-Jul-26**	5	8/3/2026				
	Install Formwork Moment Slab	**28-Jul-26**	20	8/24/2026				
	Install Rebar for Approach	**28-Jul-26**	5	8/3/2026				
	Install Rebar for Moment Slab	**28-Jul-26**	20	8/24/2026				
	Place Approach	**3-Aug-26**	1	8/3/2026				
	Place Moment Slab	**30-Jul-26**	20	8/26/2026				
	Cure Approach	**3-Aug-26**	7	8/11/2026				
	Cure Moment Slab	**30-Jul-26**	20	8/26/2026				
	Install Mirafi, Membrane and Tensar Wall 101-102	**3-Aug-26**	5	8/7/2026				
	Process Aggregate Base	**10-Aug-26**	10	8/21/2026				
	Fine Grade	**27-Aug-26**	10	9/9/2026				
	Abutment 2							
	Install Formwork Approach Slab (West Approach)	**28-Jul-26**	5	8/3/2026				
	Install Formwork Moment Slab	**28-Jul-26**	20	8/24/2026				
	Install Rebar for Approach	**28-Jul-26**	5	8/3/2026				
	Install Rebar for Moment Slab	**28-Jul-26**	20	8/24/2026				
	Place Approach	**3-Aug-26**	1	8/3/2026				
	Place Moment Slab	**30-Jul-26**	20	8/26/2026				
	Cure Approach	**3-Aug-26**	7	8/11/2026				
	Cure Moment Slab	**30-Jul-26**	30	9/9/2026				
	Bridge 00161							
	Install Integrated Approach - Partial Height	**4-May-26**	60	7/24/2026				
	Install Deck & Backwall Rebar	**15-Jun-26**	15	7/3/2026				
	Set AirSeeed / Dry run	**6-Jul-26**	2	7/7/2026				
	Place Bridge Slab & Backwall	**8-Jul-26**	1	7/8/2026				
	Cure Bridge Slab & Backwall	**8-Jul-26**	10	7/21/2026				
	Place Backwall (AB 1)	**15-Jul-26**	1	7/15/2026				
	Cure Backwall (AB 1)	**15-Jul-26**	7	7/23/2026				
	Complete Integrated Approach	**22-Jul-26**	5	7/28/2026				
	Install Formwork for Bridge Barrier	**20-Jul-26**	10	7/31/2026				
	Install Rebar For Bridge Barrier	**20-Jul-26**	7	7/28/2026				
	Apply Waterproof Membrane	**22-Jul-26**	2	7/23/2026				
	Place Bridge Barrier	**30-Jul-26**	1	7/30/2026				
	Cure Bridge Barrier	**30-Jul-26**	7	8/7/2026				
	Sheeting							
	Remove Sheeting and H pile Wall 201-201	**26-Jul-26**	10	8/6/2026	Night	2		
	Remove Sheeting and H pile Wall 101	**3-Aug-26**	15	8/23/2026	Night	2		
	Retaining Walls							
	Wall 202 to Full Height	**26-May-26**	50	8/3/2026				
	Wall 102 to Full Height	**26-May-26**	50	8/3/2026				
	Wall 101 to Full Height	**26-May-26**	40	7/20/2026				
	Wall 302 to Partial Height	**26-May-26**	50	8/3/2026				
	Wall 501 Sta 102.79-Sta. 103.53							
	Finish Pouring Moment Slab	**23-Jul-26**	1	7/23/2026				
	Cure Moment Slab	**23-Jul-26**	7	7/31/2026				
	Place Membrane	**30-Jul-26**	1	7/30/2026				
	Set Parapet Transition Ends	**4-Aug-26**	5	8/10/2026				
	Subcontractor Work							
	Saw Cut for Road Limits and Drainage	**9-Jul-26**	1	7/9/2026	Night	2		
	Electric	**15-Jun-26**	60	9/4/2026				
	Light pole base installation	**22-Jun-26**	15	7/13/2026				
	Conduit Installation	**24-Jun-26**	15	7/15/2026				
	94+00 to 123+00	Dates in process with contractor (ETC)						
	Gore Area							
	First Avenue							
	IMS Installation							
	Guard Rail	**10-Sep-26**	5	9/16/2026	Night	2		
	126+80 to 127+60	Dates in process with contractor (Quaker)						
	Exit Ramp 705+50 to 709+60							
	Signage (94+00 to 128+00)	**25-Aug-26**	5	8/31/2026	Night	2		
	Paving				Night	2		
	Initial Meeting With Waters about Paving	**22-Jun-26**	1	6/22/2026				
	98+30 to 101+03	**16-Sep-26**	8	9/25/2026				
	102+14 to 107+25	**16-Sep-26**	8	9/25/2026				
	Gore 107+25 to 110+57 and 700+00 to 704+50	**16-Sep-26**	8	9/25/2026				
	107+25 to Bridge 162 Approach Slab 114+50	**31-Aug-26**	8	9/9/2026				
	Bridge 162 Approach Slab 116+14 to Station 123+00	**31-Aug-26**	8	9/9/2026				
	Exit Ramp 704+50 to 709+00	**31-Aug-26**	8	9/9/2026				
	Line Striping	**16-Sep-26**	2	9/17/2026	Night	2		
	94+00 to 128+00 and Exit Ramp	Dates coincide with paving						
	Traffic Switch	**18-Sep-26**	8	9/28/2026	Night	3		
	Traffic Switch 2.1	**10-Sep-26**	1	9/10/2026				
	Traffic Switch 2.2	**26-Sep-26**	3	9/29/2026				
	Subcontractors							
	Designs by Ilde - E&S Control							
	Alvarez- Rebar Installation							
	ETC- Temp Lighting							
	Fareos Trucking							
	A& R Trucking							

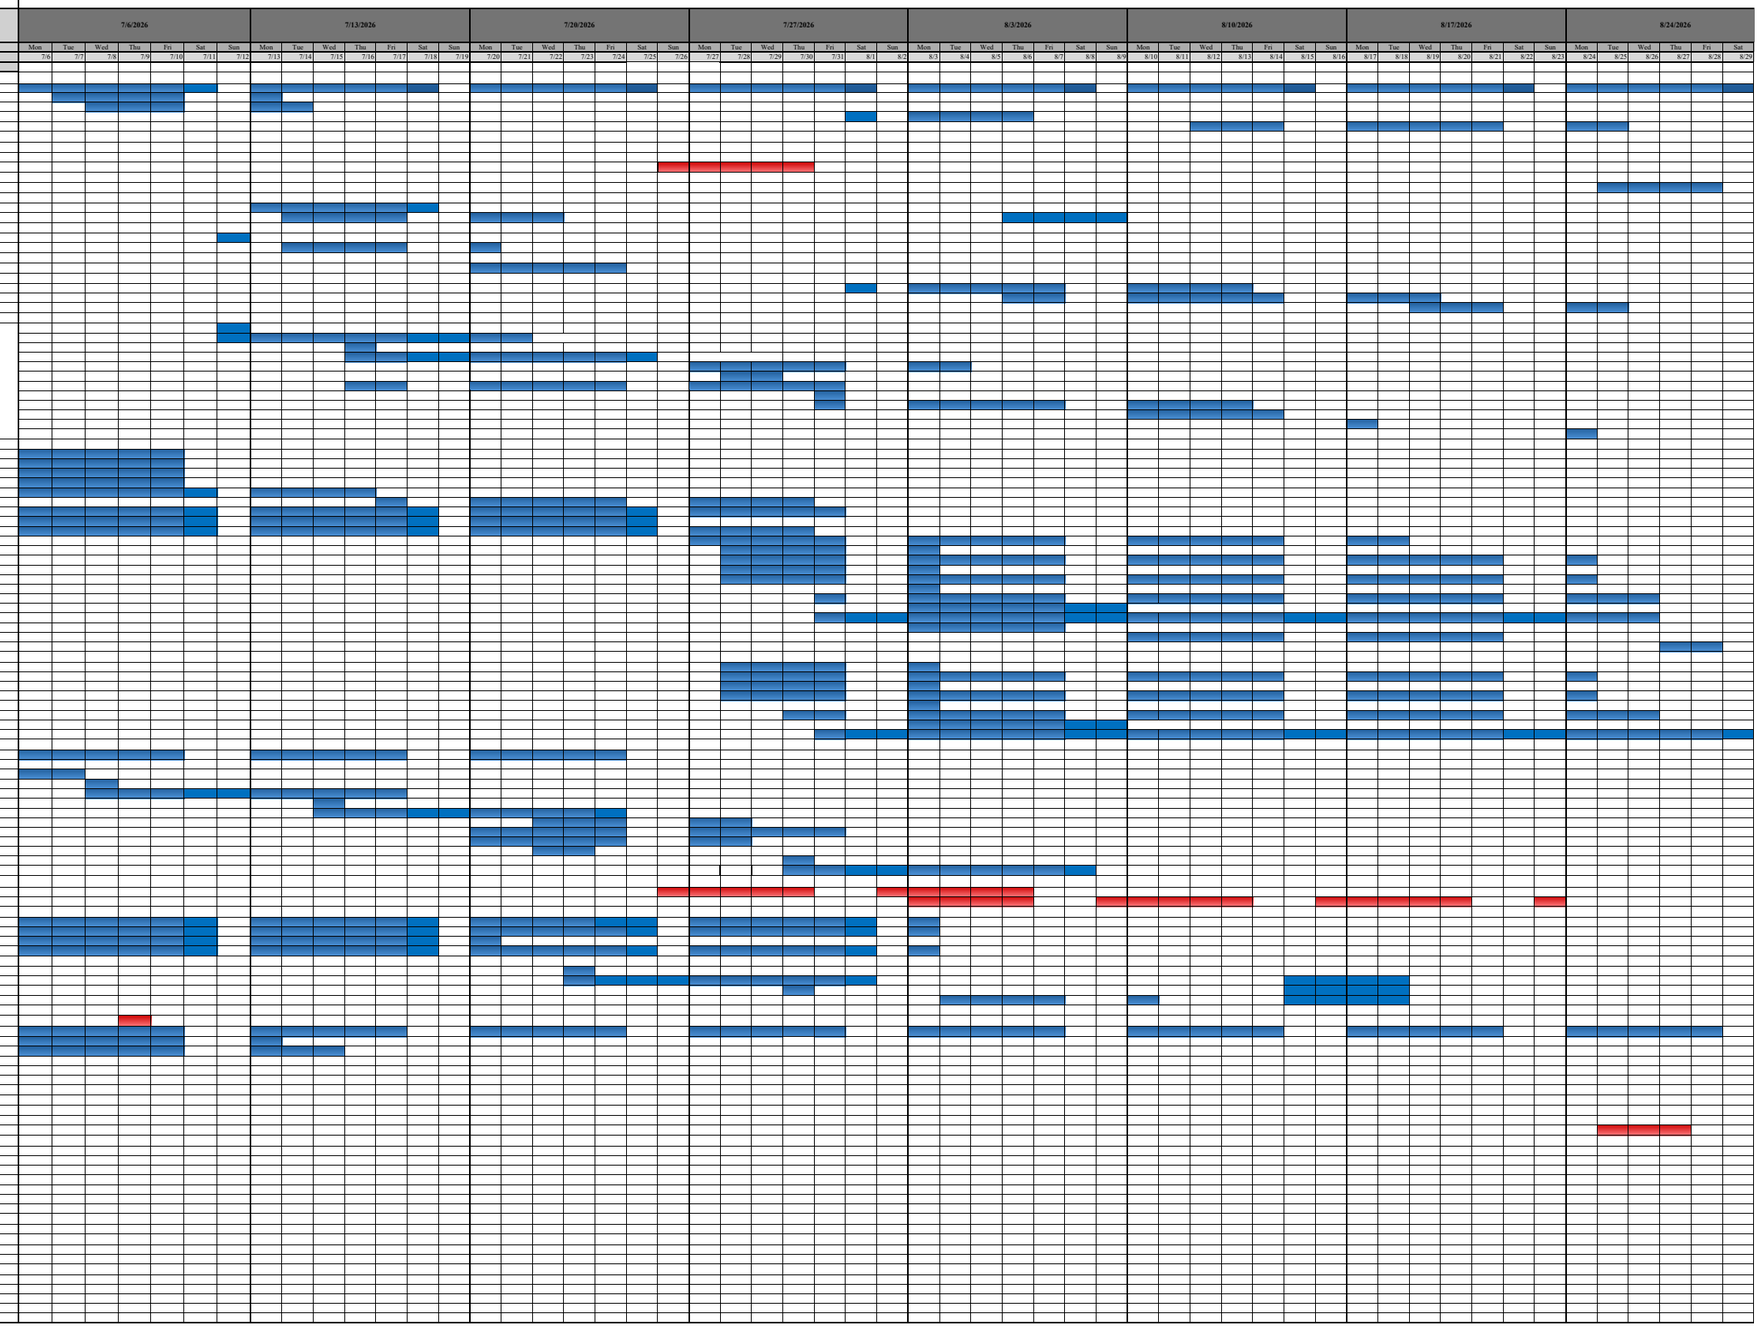

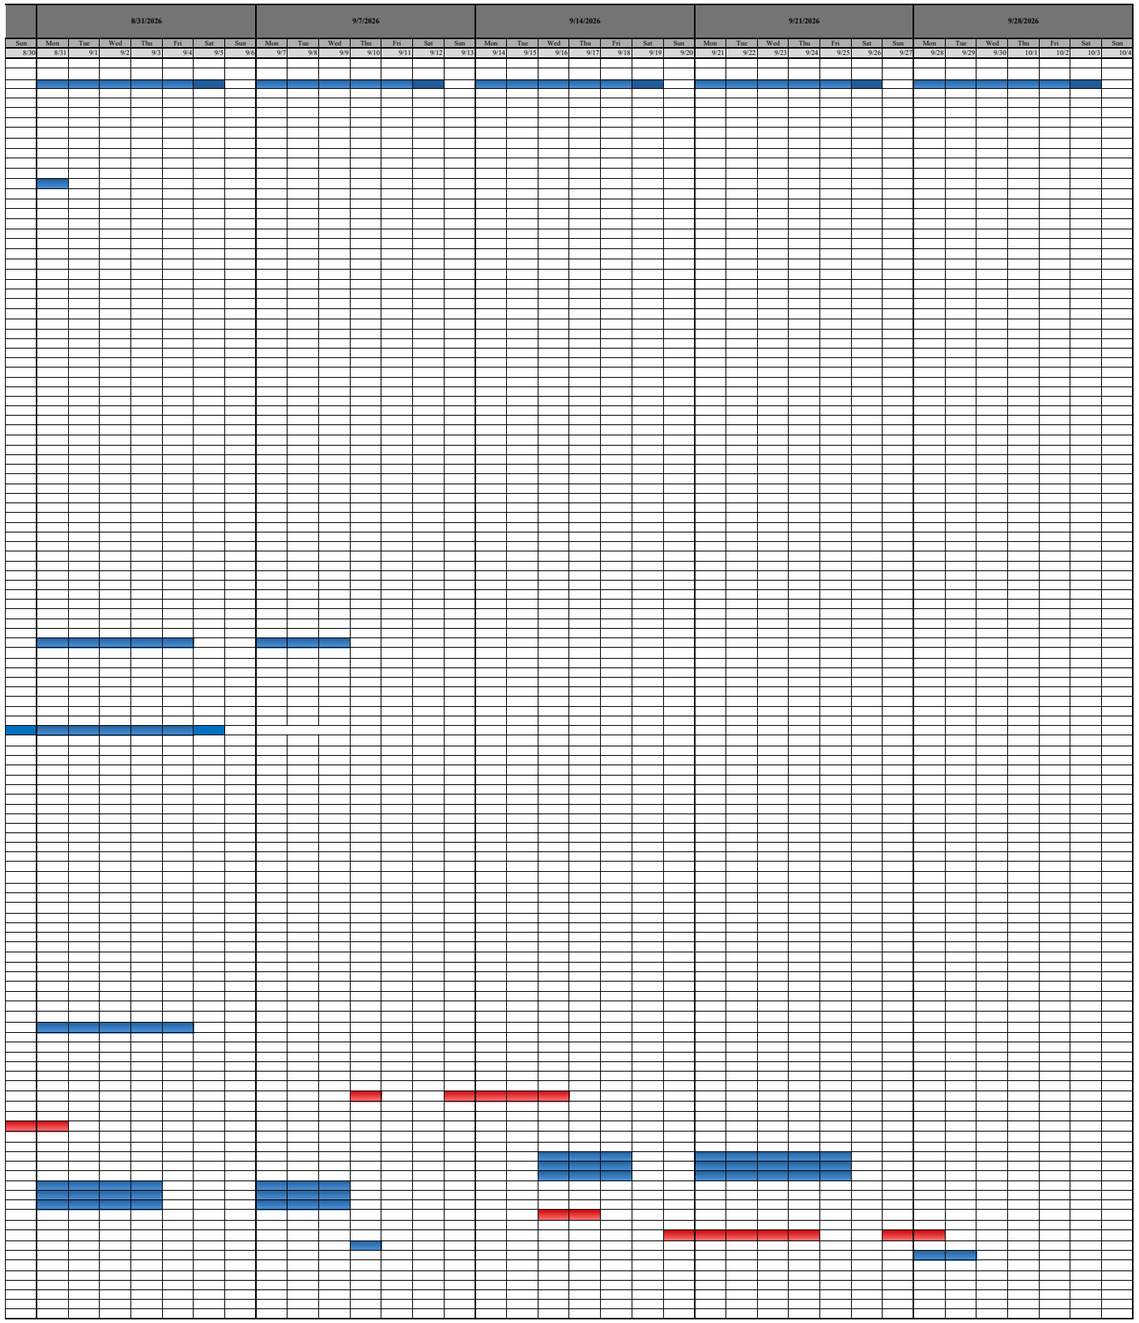
8/31/2026
9/7/2026
9/14/2026
9/21/2026
9/28/2026
Sun Mon Tue Wed Thu Fri Sat Sun Mon Tue Wed Thu Fri Sat Sun Mon Tue Wed Thu Fri Sat Sun Mon Tue Wed Thu Fri Sat Sun Mon Tue Wed Thu Fri Sat Sun
8/30 8/31 9/1 9/2 9/3 9/4 9/5 9/6 9/7 9/8 9/9 9/10 9/11 9/12 9/13 9/14 9/15 9/16 9/17 9/18 9/19 9/20 9/21 9/22 9/23 9/24 9/25 9/26 9/27 9/28 9/29 9/30 10/1 10/2 10/3 10/4
