The Middlesex Corporation

90 Day Look Ahead

Input Date of First Monday
8/3/2026

Item #	Activity Description	Start Date	Working Days	End Date	Shift	State Police	Local Police	MNR Support
	Look Ahead Schedule							
	Project							
	Replacement of Bridges 00161 & 00162							
	Construction							
	Install/Repair Silt Fence site wide as Needed	**5-Jan-26**	190	9/25/2026				
	Remove Invasives	**27-Jul-26**	35	9/11/2026				
	Deliveries of FGA to Resume 1 load per day	**27-Jul-26**	135	1/29/2027				
	Remove Aphalt and Road Base to Phase Line 202	**29-Jul-26**	35	9/15/2026	Night	2		
	Drainage							
	Highway							
	Extend RCP for Next Phase DS 3, 33 and 37	**29-Jul-26**	5	8/4/2026				
	West Side of Wall 202							
	Water Quality Area 3	**25-Aug-26**	5	8/31/2026				
	Gore/Grass Area Drainage							
	Install 24" From DS- 45 to DS- 29 (15' Deep)	**27-Jul-26**	10	8/7/2026				
	Install DS- 43 and 24"RCP	**10-Aug-26**	5	8/14/2026				
	West Side of Exit and Through Exit Ramp 43							
	Demo Head Wall and Pipe	**27-Jul-26**	1	7/27/2026				
	Scour Hole Headwall and Drainage Across Exit Ramp	**28-Jul-26**	5	8/3/2026	Night	2		
	First Ave Drainage							
	Install DS- 42A and 42B, EX MH 6, 57	**9-Oct-26**	5	10/15/2026				
	Crossing First Ave	**13-Oct-26**	3	10/15/2026	Night	2		
	Commuter Lot Area							
	DS- 57-17, 17-16, 17-15, 15-14, 13, 19, 18	**13-Oct-26**	20	11/9/2026				
	400' +/- RCP Pipe	**14-Oct-26**	10	10/27/2026				
	Water Quality Area 1 Plus Liner	**19-Oct-26**	5	10/23/2026				
	Bridge 00162							
	Form Bridge Barrier	**20-Jul-26**	10	7/31/2026				Flagger
	Rebar for Bridge Barrier	**27-Jul-26**	10	8/7/2026				
	Place Bridge Barrier (Parapet)	**1-Aug-26**	2	8/3/2026				
	Cure Bridge Barrier (Parapet)	**1-Aug-26**	7	8/10/2026				
	Apply Waterproof Membrane for Slab	**28-Sep-26**	2	9/29/2026				
	Abutment 1							
	Parapet Level Pad	**16-Jul-26**	45	9/16/2026				
	Place FGA Wall 102	**30-Jul-26**	39	9/22/2026				
	Install Panels and Light Weight Wall 102	**6-Aug-26**	30	9/16/2026				
	Continue Installing Phase Line Wall	**6-Aug-26**	35	9/23/2026				
	Parapet Delivery	**6-Aug-26**	30	9/16/2026	Night	2		
	Set Parapet	**7-Aug-26**	30	9/17/2026				
	Prep for Moment Slab	**10-Aug-26**	30	9/18/2026				
	Install Formwork Moment Slab (West Approach)	**11-Aug-26**	30	9/21/2026				
	Install Rebar for Moment Slab	**12-Aug-26**	30	9/22/2026				
	Place Moment Slab	**14-Aug-26**	30	9/24/2026				
	Cure Moment Slab (Per Section)	**14-Aug-26**	35	10/1/2026				
	Install Mirafi, Membrane and Tensar Wall 101-102	**15-Aug-26**	35	10/1/2026				
	Process Aggregate Base	**17-Aug-26**	35	10/2/2026				
	Fine Grade	**27-Aug-26**	35	10/14/2026				
	Abutment 2							
	Form Level up Concrete	**14-May-26**	60	8/5/2026				
	Pour Levelling Pad	**22-May-26**	60	8/13/2026				
	Set Parapets	**9-Jun-26**	65	9/7/2026				
	Install Formwork Moment Slab (East Approach)	**12-Jun-26**	40	8/6/2026				
	Install Rebar for Moment Slab	**12-Jun-26**	64	9/9/2026				
	Place Moment Slab	**27-Jun-26**	55	9/10/2026				
	Cure Moment Slab (Per Section)	**27-Jun-26**	60	9/17/2026				
	Prep Approach Slab	**3-Aug-26**	3	8/5/2026				
	Form Approach Slab	**5-Aug-26**	2	8/6/2026				
	Install Rebar Approach Slab	**7-Aug-26**	3	8/11/2026				
	Pour Approach Slab	**10-Aug-26**	1	8/10/2026				
	Cure Approach Slab	**10-Aug-26**	7	8/18/2026				
	Bridge 00161							
	Install Formwork for Bridge Barrier	**20-Jul-26**	10	7/31/2026				
	Install Rebar For Bridge Barrier	**20-Jul-26**	7	7/28/2026				
	Form and Pour End Block (North Side)	**30-Jul-26**	25	9/2/2026				
	Place Bridge Barrier	**30-Jul-26**	30	9/9/2026				
	Cure Bridge Barrier	**31-Jul-26**	35	9/17/2026				
	Sheeting/Saw Cutting							
	Load/Haul Sheets to Sackett Point	**1-Aug-26**	35	9/17/2026				
	Remove Sheeting and H pile Wall 201-201	**6-Jul-26**	50	9/13/2026	Night	2		
	Saw Cut Remaining Asphalt 101 and 202	**28-Sep-26**	2	9/29/2026				
	Retaining Walls							
	Wall 202 to Full Height	**26-May-26**	60	8/17/2026				
	Wall 102 to Full Height	**26-May-26**	80	9/14/2026				
	Wall 501 Sta 102.79-Sta. 103.53							
	Transition Pieces Installed	**15-Sep-26**	2	9/16/2026				
	Form Moment	**17-Aug-26**	25	9/18/2026				
	Install Rebar	**18-Aug-26**	25	9/21/2026				
	Pour Moment slab	**18-Sep-26**	1	9/18/2026				
	Cure Moment Slab	**18-Sep-26**	7	9/28/2026				
	Install Membrane and Road Base	**1-Oct-26**	1	10/1/2026				
	Subcontractor Work							
	Electric	**15-Jun-26**	80	10/2/2026				
	94+00 to 123+00	**1-Jul-26**	75	10/13/2026				
	Light pole base installation	**22-Jun-26**	60	9/14/2026				
	Conduit Installation	**24-Jun-26**	65	9/23/2026				
	Gore Area	**1-Jul-26**	55	9/16/2026				
	IMS Installation	**14-Sep-26**	25	10/16/2026				
	Guard Rail	**26-Oct-26**	10	11/8/2026	Night	2		
	126+80 to 127+60	**26-Oct-26**	5	10/30/2026				
	Exit Ramp 705+50 to 709+60	**1-Nov-26**	6	11/6/2026				
	Signage	**25-Oct-26**	5	10/29/2026	Night	2		
	94+00 to 128+00							
	Paving	**18-Oct-26**	8	10/27/2026	Night	2		
	Initial Meeting With Waters about Paving	**22-Jun-26**	1	6/22/2026	Night			
	Bridge 162 Approach Slab 116+14 to Station 123+00	**1-Oct-26**	5	10/7/2026	Night			
	107+25 to Bridge 162 Approach Slab 114+50	**7-Oct-26**	5	10/13/2026	Night			
	Exit Ramp 704+50 to 709+00	**7-Oct-26**	5	10/13/2026	Night			
	98+30 to 101+03	**14-Oct-26**	4	10/19/2026	Night			
	102+14 to 107+25	**19-Oct-26**	5	10/25/2026	Night			
	Gore 107+25 to 110+57 and 700+00 to 704+50	**19-Oct-26**	5	10/25/2026	Night			
	First Avenue							
	Line Striping	**16-Sep-26**	2	9/17/2026	Night	2		
	94+00 to 128+00 and Exit Ramp							
	First Avenue							
	Traffic Switch	**20-Oct-26**	13	11/5/2026	Night	3		
	Move/Set Barrier 2A	**20-Oct-26**	5	10/26/2026				
	Move/Set Barrier 2	**30-Oct-26**	5	11/5/2026				
	Subcontractors							
	Alvarez- Rebar Installation	**22-Jun-26**		9/22/2026				
	ETC- Temp Lighting	**15-Jun-26**	80	10/2/2026				
	Vinagro- Bridge Demo	**9-Nov-26**	21	12/7/2026				
	A&R Trucking	**5-Jan-26**	200	10/9/2026				

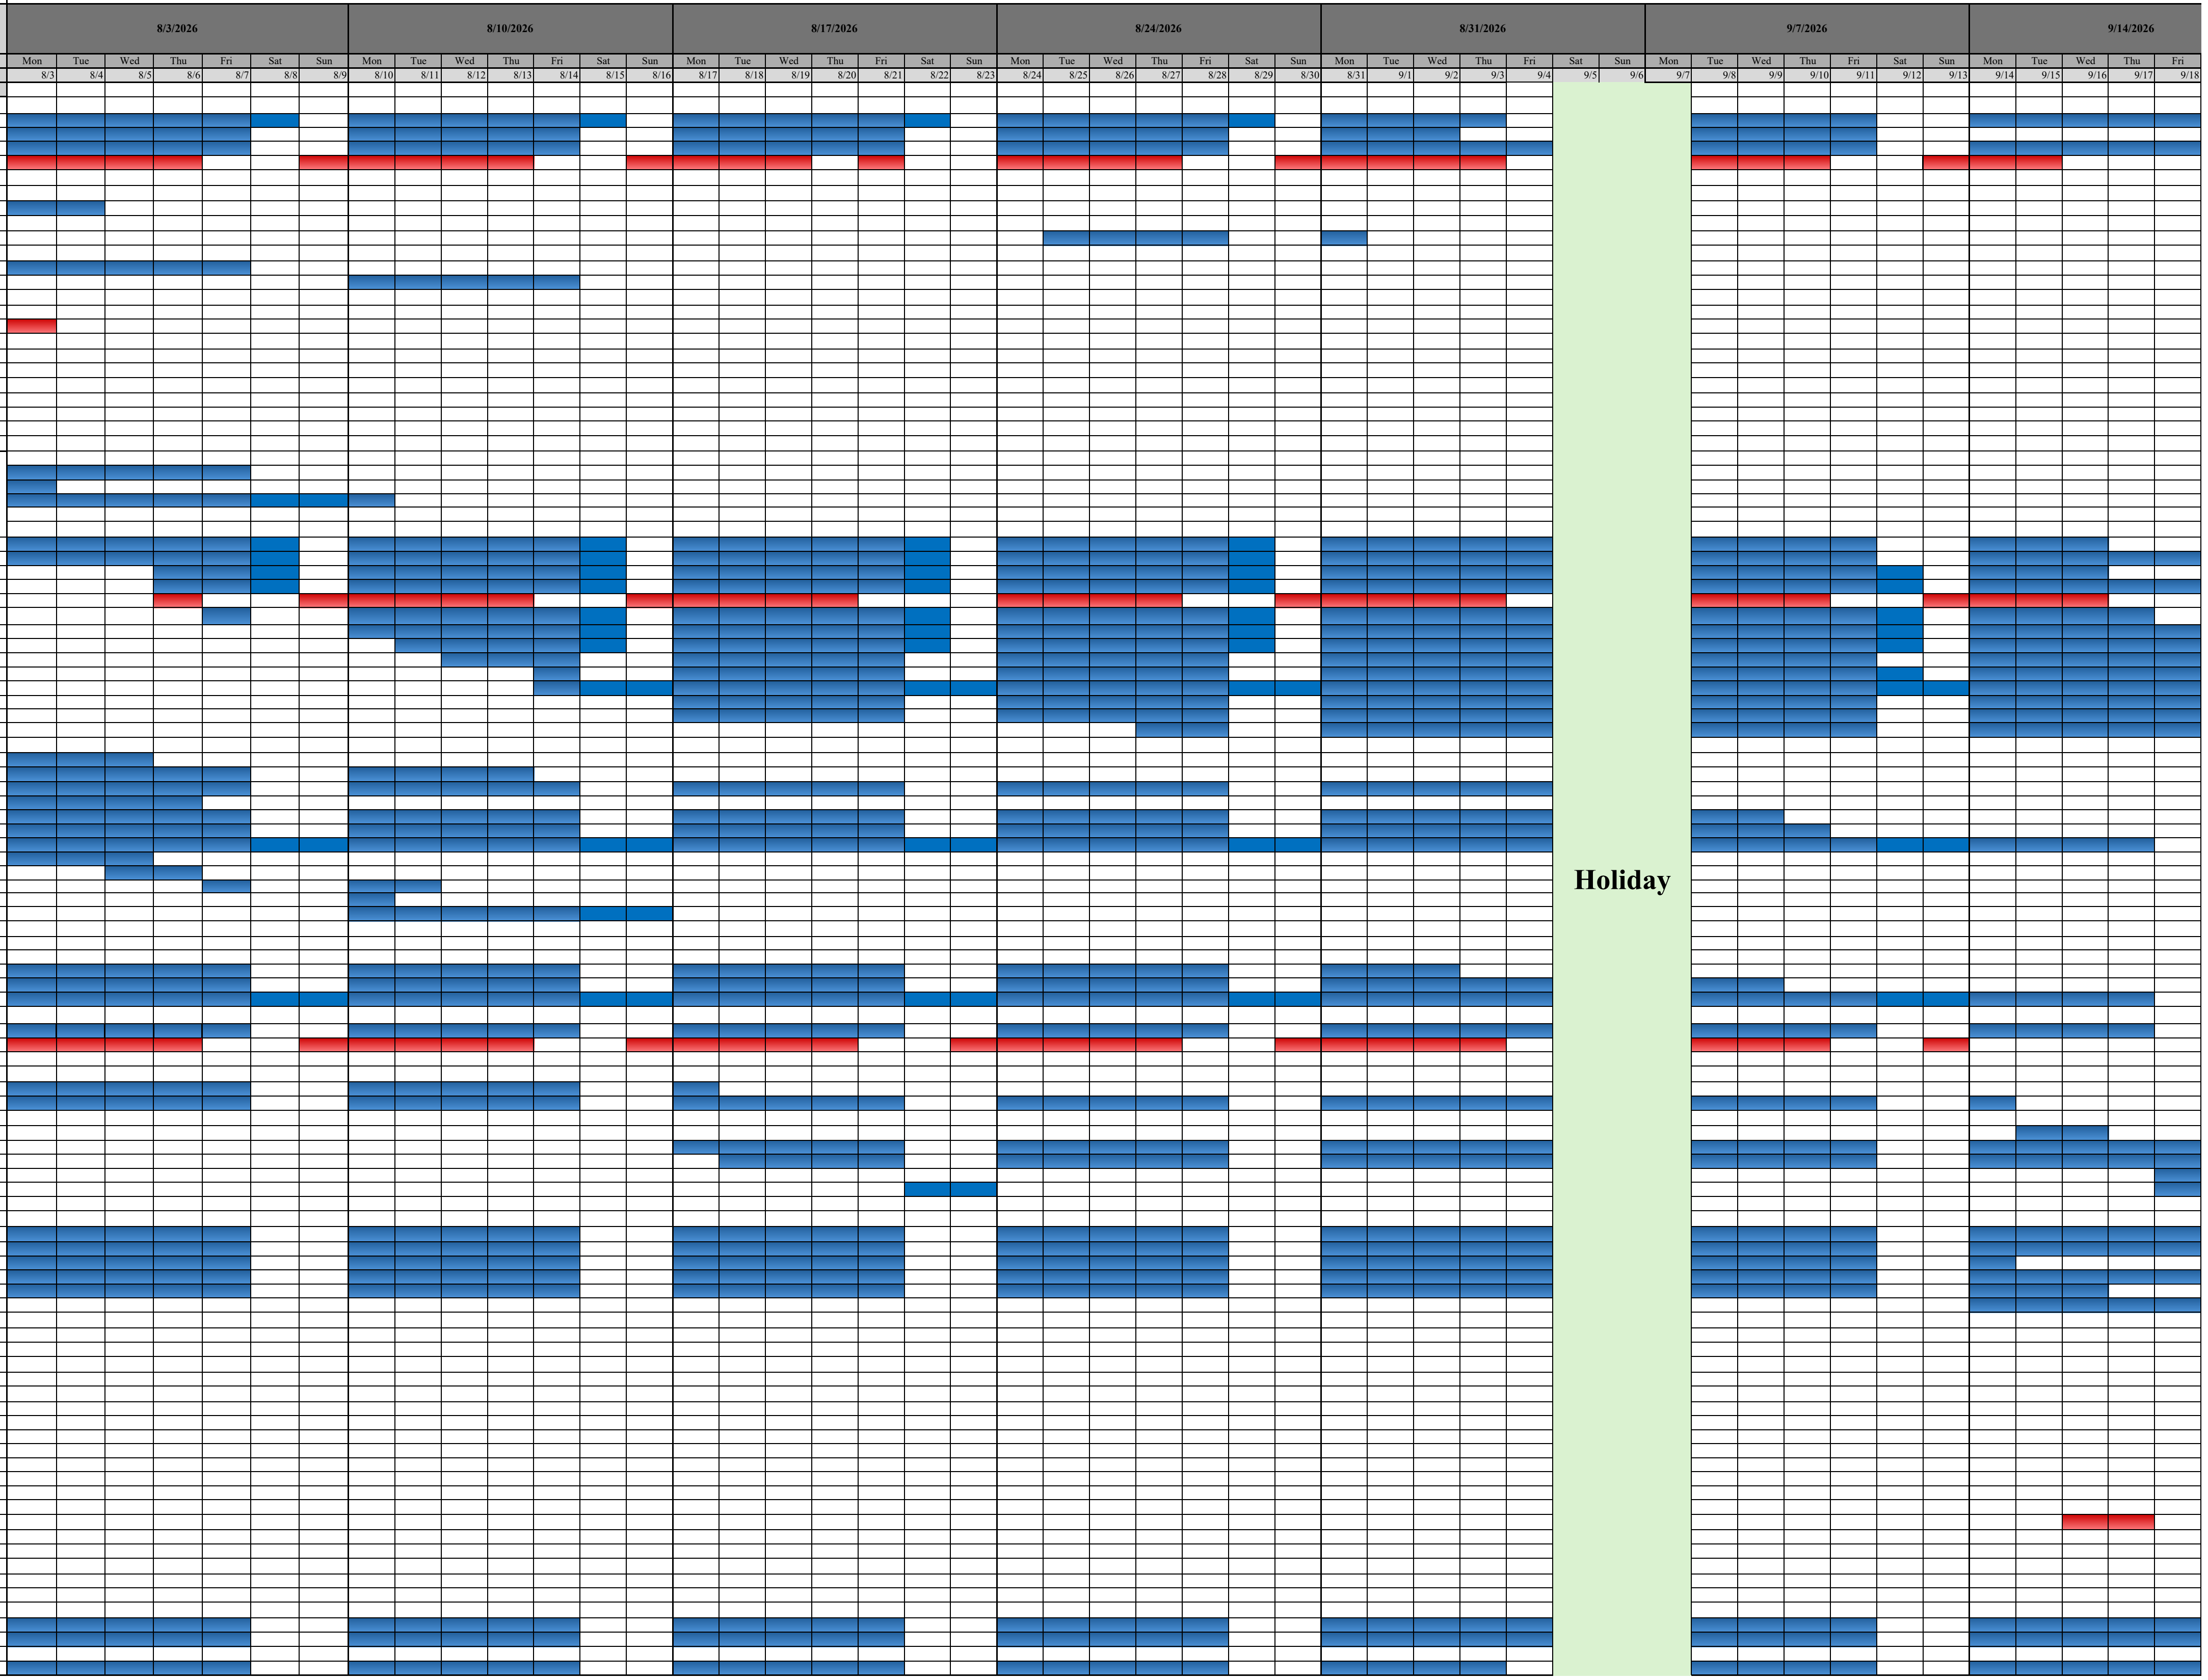

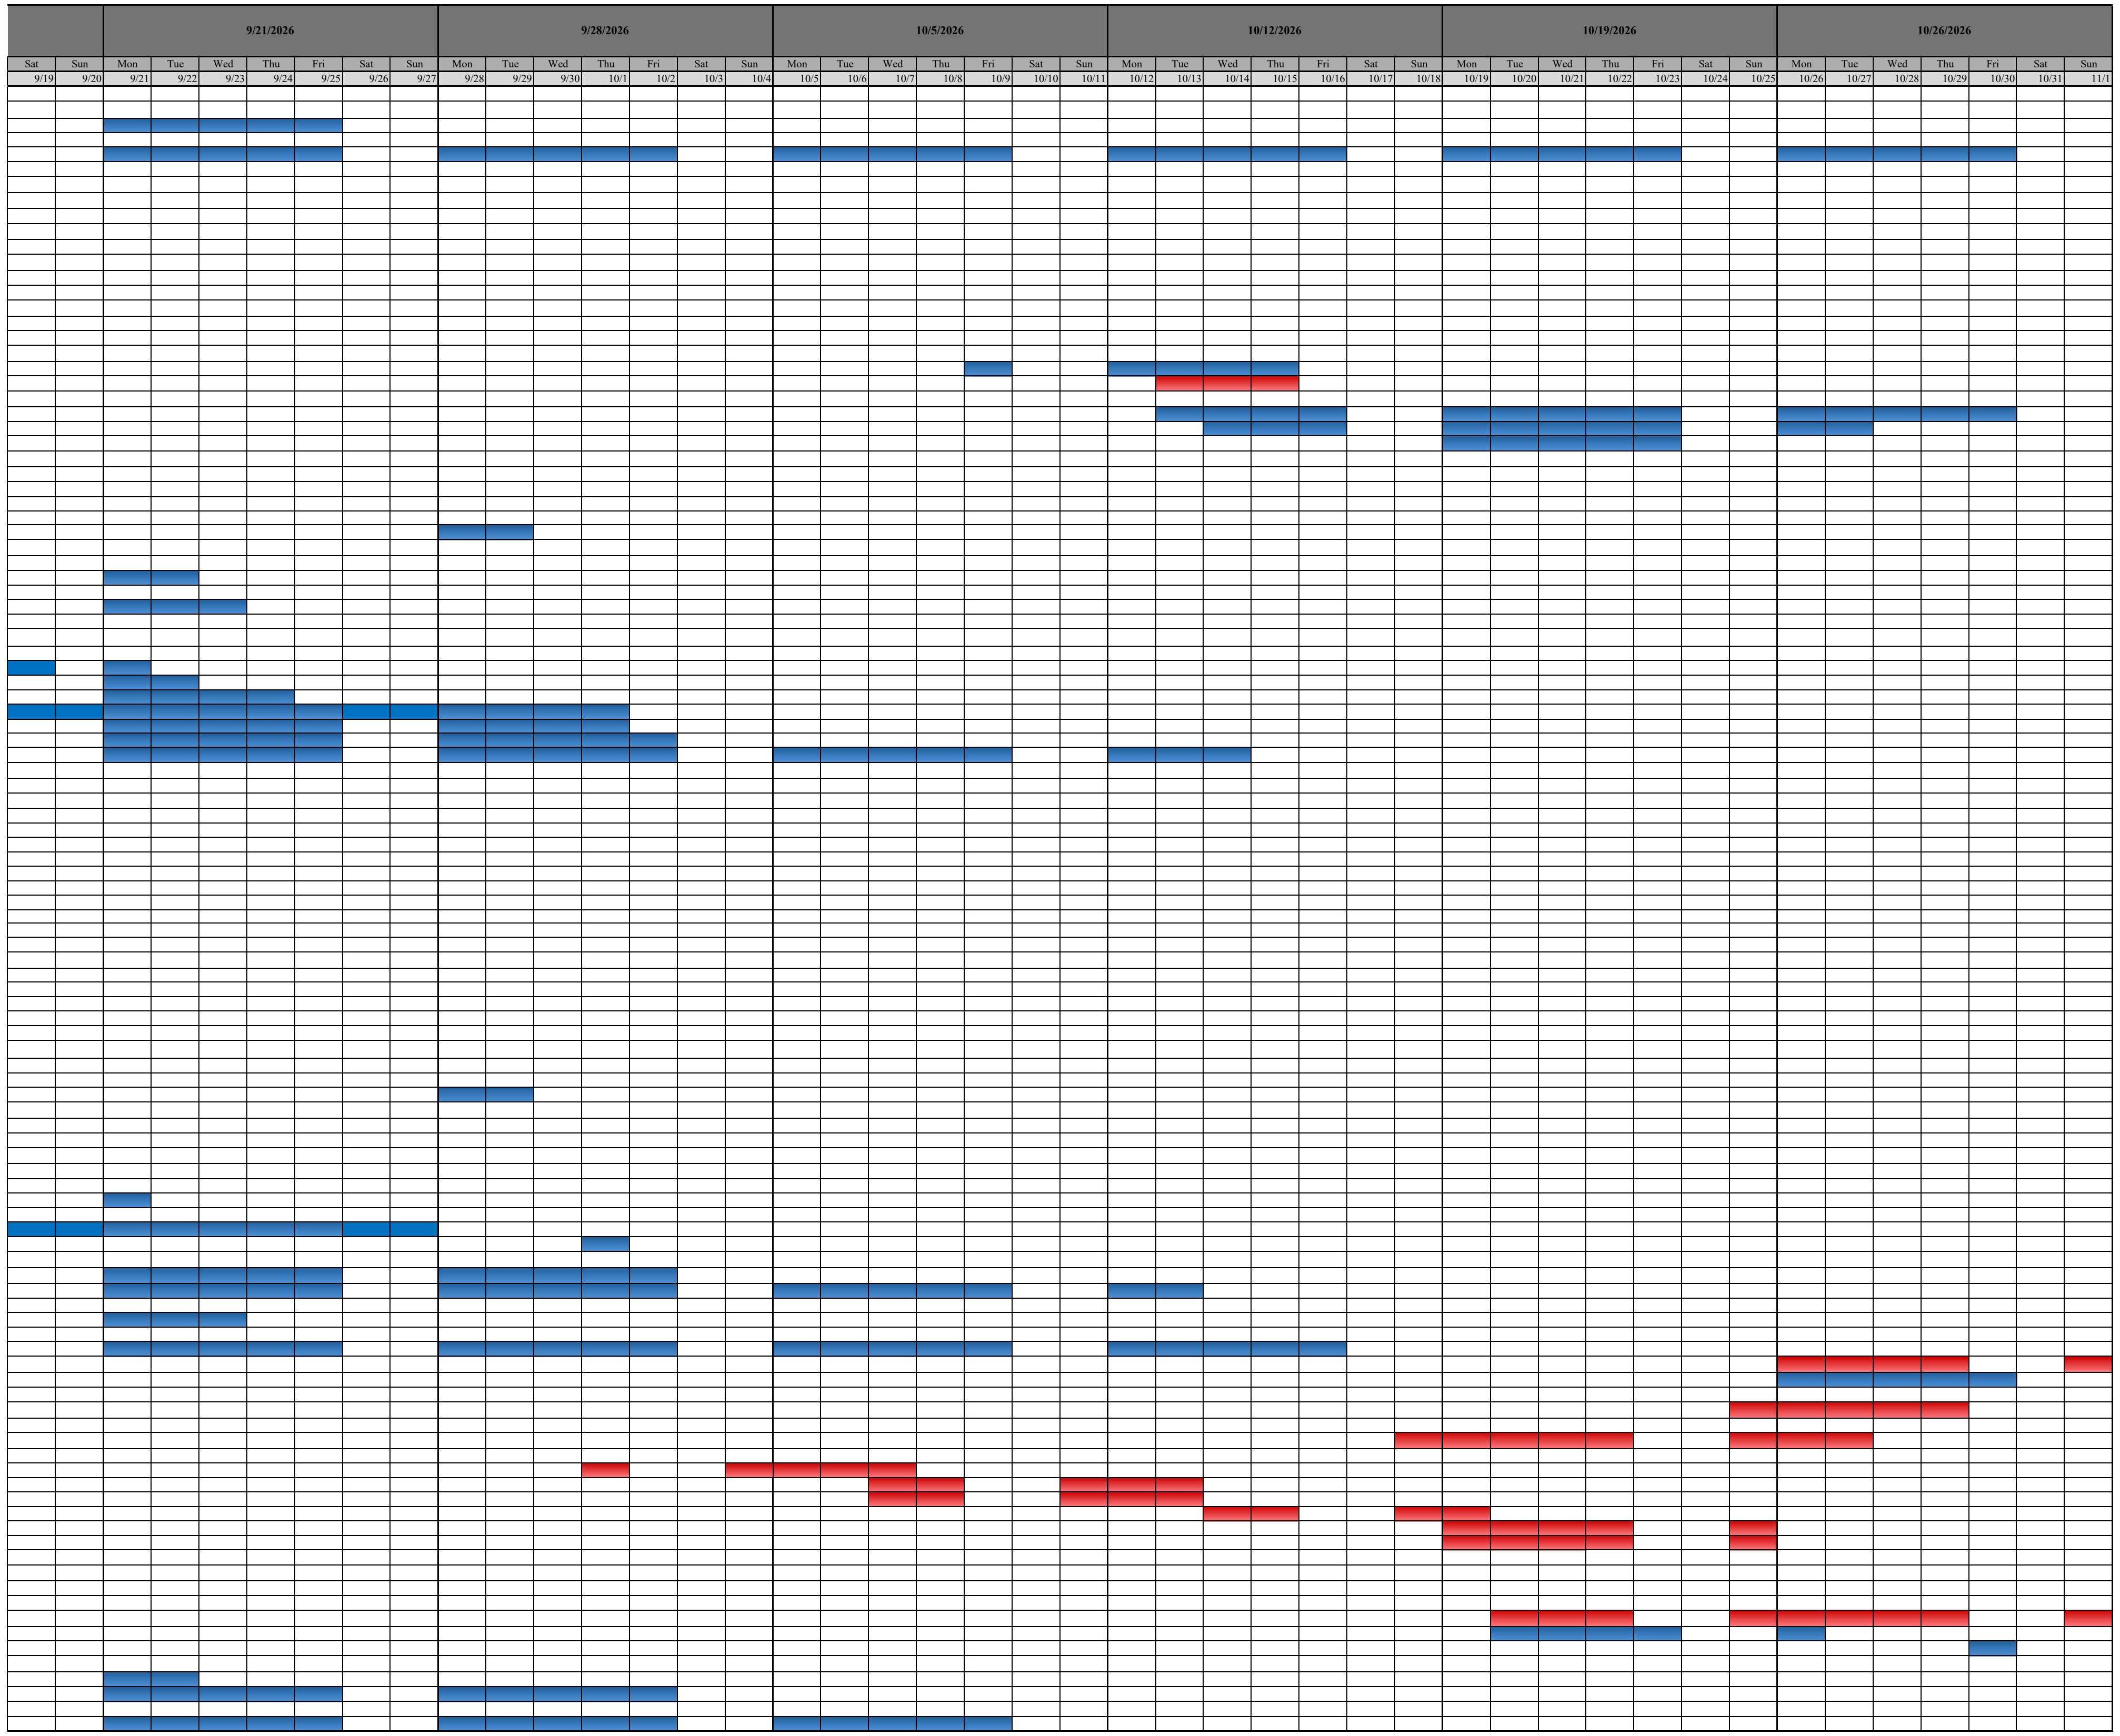
9/21/2026
9/28/2026
10/5/2026
10/12/2026
10/19/2026
10/26/2026
Sat 9/19
Sun 9/20
Mon 9/21
Tue 9/22
Wed 9/23
Thu 9/24
Fri 9/25
Sat 9/26
Sun 9/27
Mon 9/28
Tue 9/29
Wed 9/30
Thu 10/1
Fri 10/2
Sat 10/3
Sun 10/4
Mon 10/5
Tue 10/6
Wed 10/7
Thu 10/8
Fri 10/9
Sat 10/10
Sun 10/11
Mon 10/12
Tue 10/13
Wed 10/14
Thu 10/15
Fri 10/16
Sat 10/17
Sun 10/18
Mon 10/19
Tue 10/20
Wed 10/21
Thu 10/22
Fri 10/23
Sat 10/24
Sun 10/25
Mon 10/26
Tue 10/27
Wed 10/28
Thu 10/29
Fri 10/30
Sat 10/31
Sun 11/1
